ID	Task Mode	Task Name	Duration	Start	Finish
1		**Buhl Infrastructure Improvements**	**70 days?**	**Fri 7/16/21**	**Thu 10/21/21**
2		Paving base course (Culver, Mine, Jones, Mercer, Pennsylvania, Alley N, Alley M)	5 days?	Mon 7/26/21	Fri 7/30/21
3		**Pennsylvania Avenue (City & County)**	**11 days**	**Fri 7/16/21**	**Fri 7/30/21**
4		Road Reconstruction	6 days	Fri 7/16/21	Fri 7/23/21
5		Concrete	4 days	Mon 7/26/21	Thu 7/29/21
6		Paving	1 day	Fri 7/30/21	Fri 7/30/21
7		**(W) Alley South of Jones**	**8 days**	**Mon 7/19/21**	**Wed 7/28/21**
8		Water	5 days	Mon 7/19/21	Fri 7/23/21
9		Sanitary Sewer	5 days	Mon 7/19/21	Fri 7/23/21
10		Alley Reconstruction	2 days	Mon 7/26/21	Tue 7/27/21
11		Concrete	1 day	Wed 7/28/21	Wed 7/28/21
12		**(F) Alley East of Roberts**	**10 days**	**Tue 7/20/21**	**Mon 8/2/21**
13		Removals	1 day	Tue 7/20/21	Tue 7/20/21
14		Water	6 days	Wed 7/21/21	Wed 7/28/21
15		Sanitary Sewer	6 days	Wed 7/21/21	Wed 7/28/21
16		Alley Reconstruction	3 days	Thu 7/29/21	Mon 8/2/21
17		**(E) Roberts Street**	**22 days**	**Mon 7/26/21**	**Tue 8/24/21**
18		Removals	2 days	Mon 7/26/21	Tue 7/27/21
19		Sanitary Sewer	7 days	Wed 7/28/21	Thu 8/5/21
20		Water	7 days	Wed 7/28/21	Thu 8/5/21
21		Storm Sewer	1 day	Fri 8/6/21	Fri 8/6/21
22		Road Reconstruction	4 days	Mon 8/9/21	Thu 8/12/21
23		Concrete	3 days	Fri 8/13/21	Tue 8/17/21

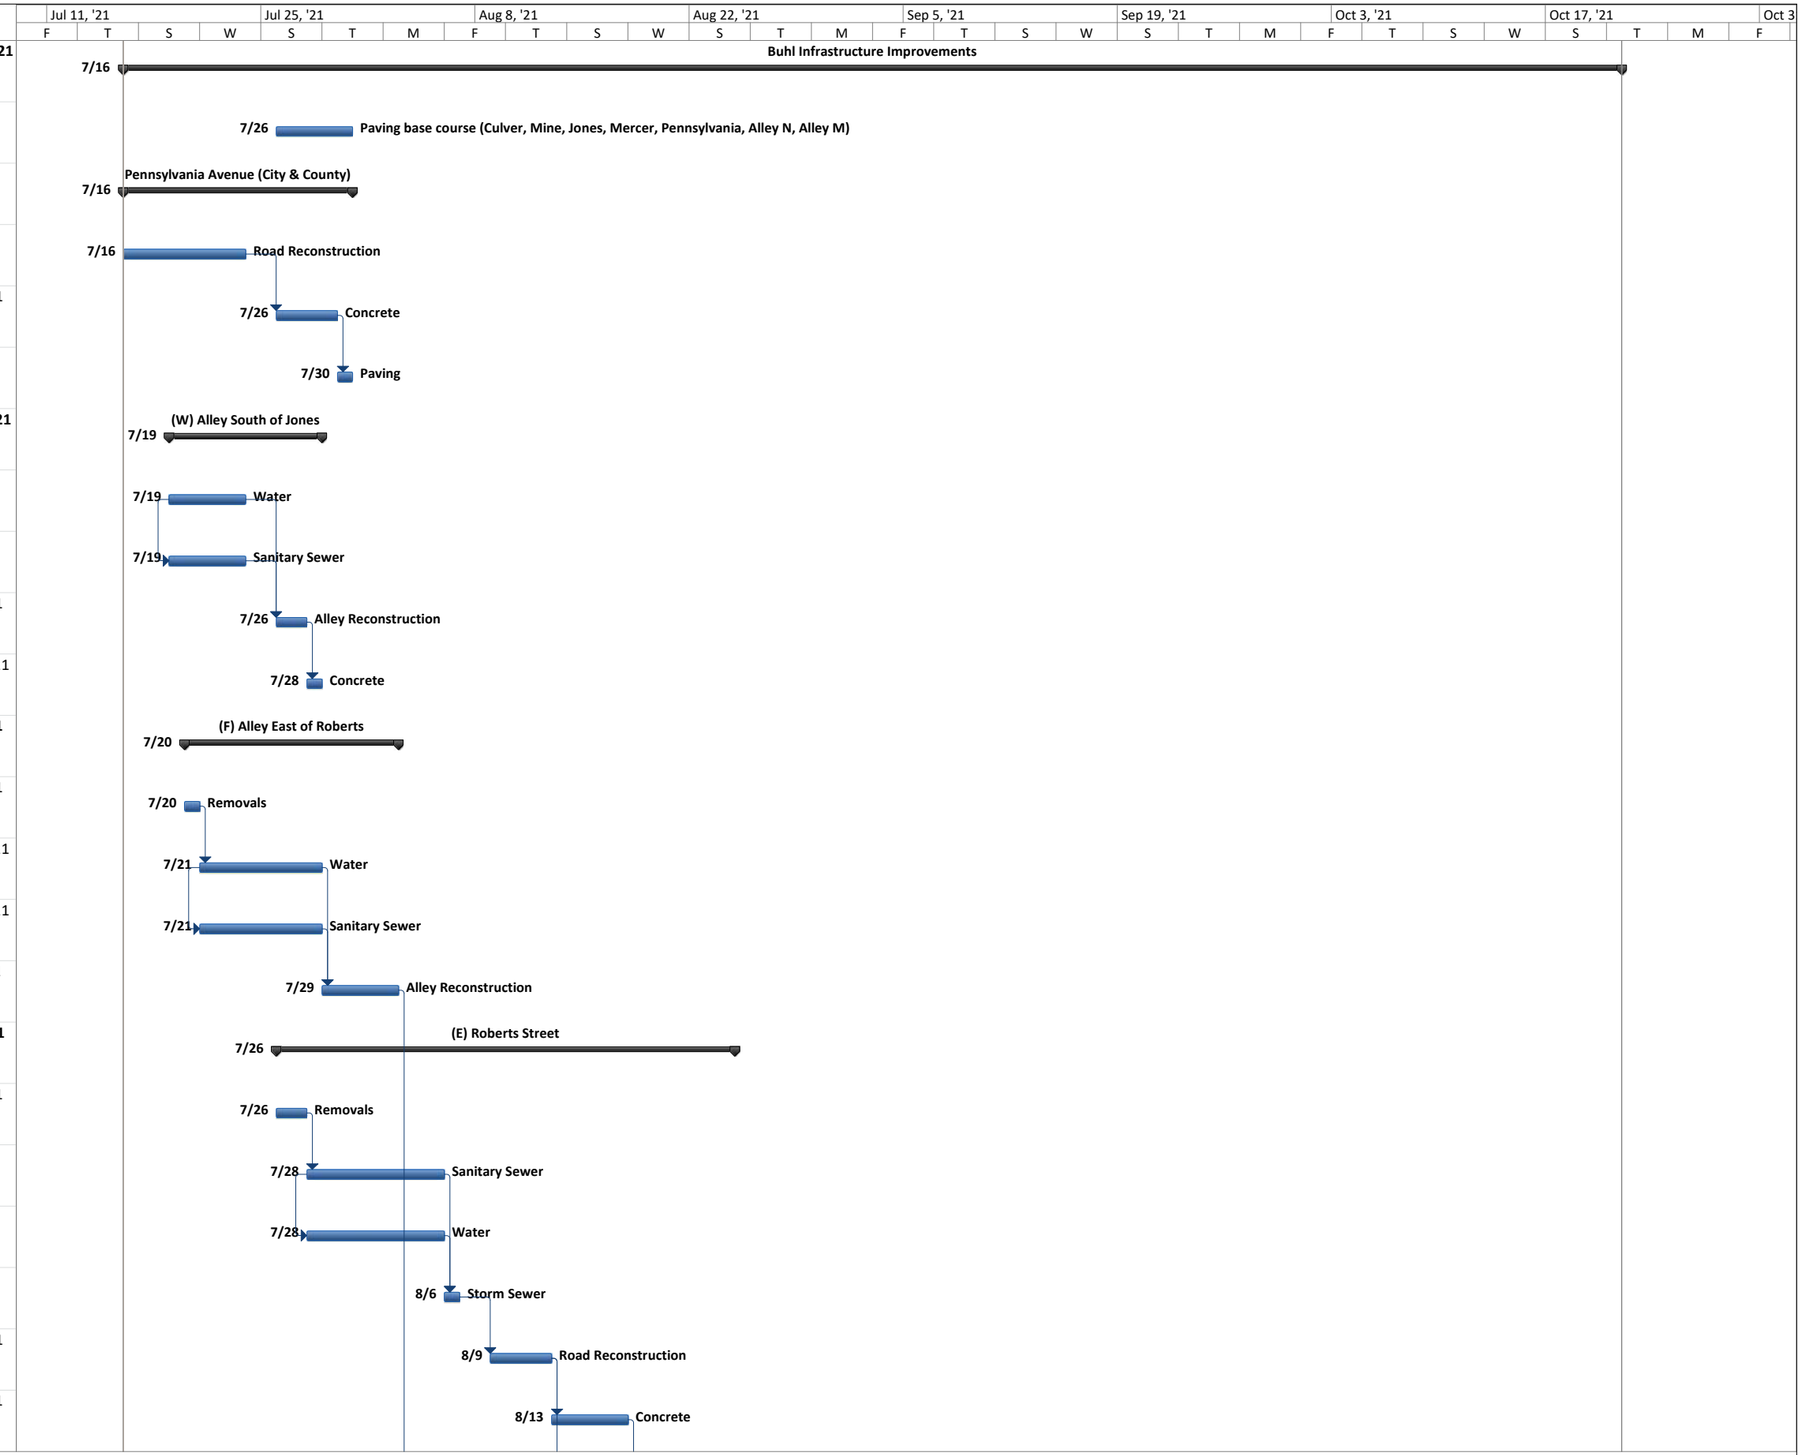
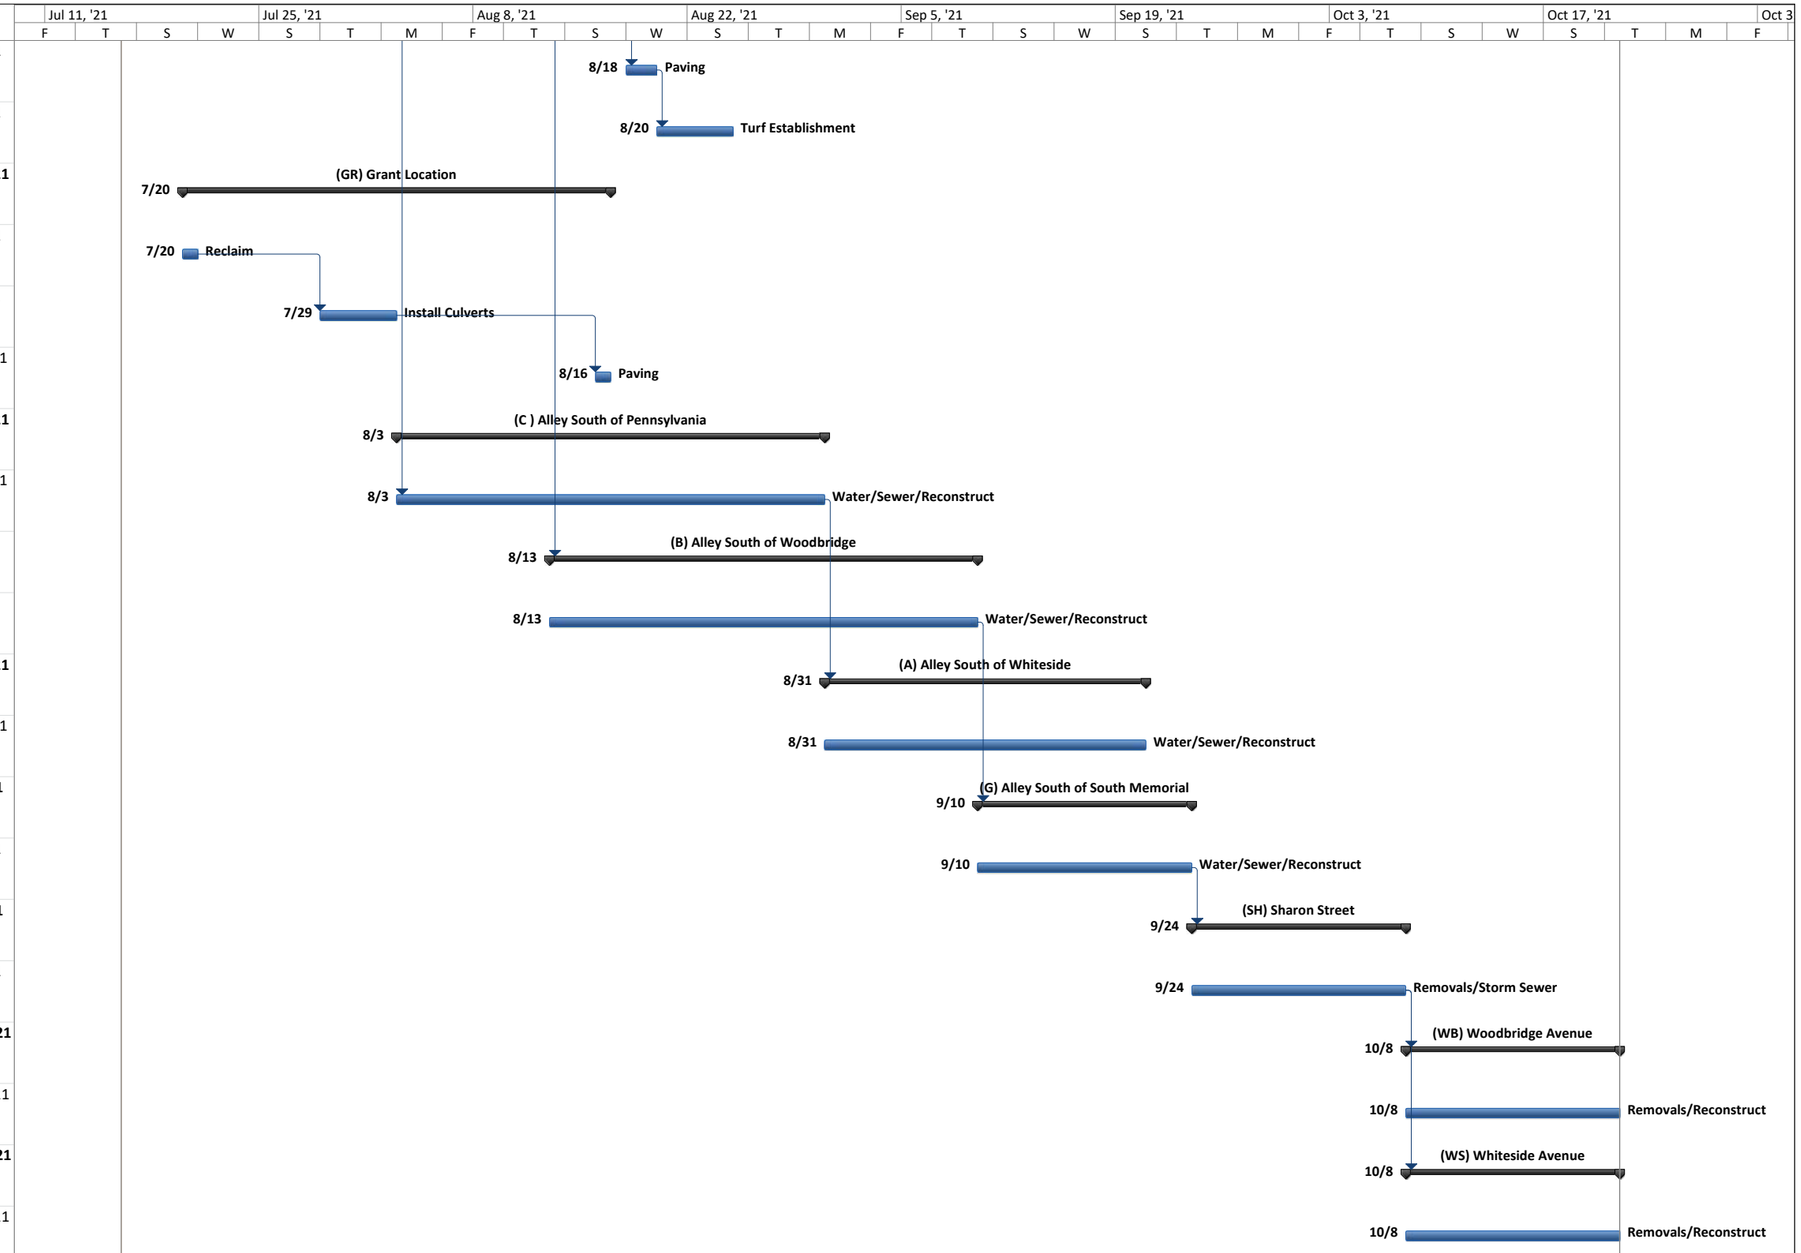
ID	Task Mode	Task Name	Duration	Start	Finish
24		Paving	2 days	Wed 8/18/21	Thu 8/19/21
25		Turf Establishment	3 days	Fri 8/20/21	Tue 8/24/21
26		**(GR) Grant Location**	**20 days**	**Tue 7/20/21**	**Mon 8/16/21**
27		Reclaim	1 day	Tue 7/20/21	Tue 7/20/21
28		Install Culverts	3 days	Thu 7/29/21	Mon 8/2/21
29		Paving	1 day	Mon 8/16/21	Mon 8/16/21
30		**(C) Alley South of Pennsylvania**	**20 days**	**Tue 8/3/21**	**Mon 8/30/21**
31		Water/Sewer/Reconstruct	20 days	Tue 8/3/21	Mon 8/30/21
32		**(B) Alley South of Woodbridge**	**20 days**	**Fri 8/13/21**	**Thu 9/9/21**
33		Water/Sewer/Reconstruct	20 days	Fri 8/13/21	Thu 9/9/21
34		**(A) Alley South of Whiteside**	**15 days**	**Tue 8/31/21**	**Mon 9/20/21**
35		Water/Sewer/Reconstruct	15 days	Tue 8/31/21	Mon 9/20/21
36		**(G) Alley South of South Memorial**	**10 days**	**Fri 9/10/21**	**Thu 9/23/21**
37		Water/Sewer/Reconstruct	10 days	Fri 9/10/21	Thu 9/23/21
38		**(SH) Sharon Street**	**10 days**	**Fri 9/24/21**	**Thu 10/7/21**
39		Removals/Storm Sewer	10 days	Fri 9/24/21	Thu 10/7/21
40		**(WB) Woodbridge Avenue**	**10 days**	**Fri 10/8/21**	**Thu 10/21/21**
41		Removals/Reconstruct	10 days	Fri 10/8/21	Thu 10/21/21
42		**(WS) Whiteside Avenue**	**10 days**	**Fri 10/8/21**	**Thu 10/21/21**
43		Removals/Reconstruct	10 days	Fri 10/8/21	Thu 10/21/21
